


177

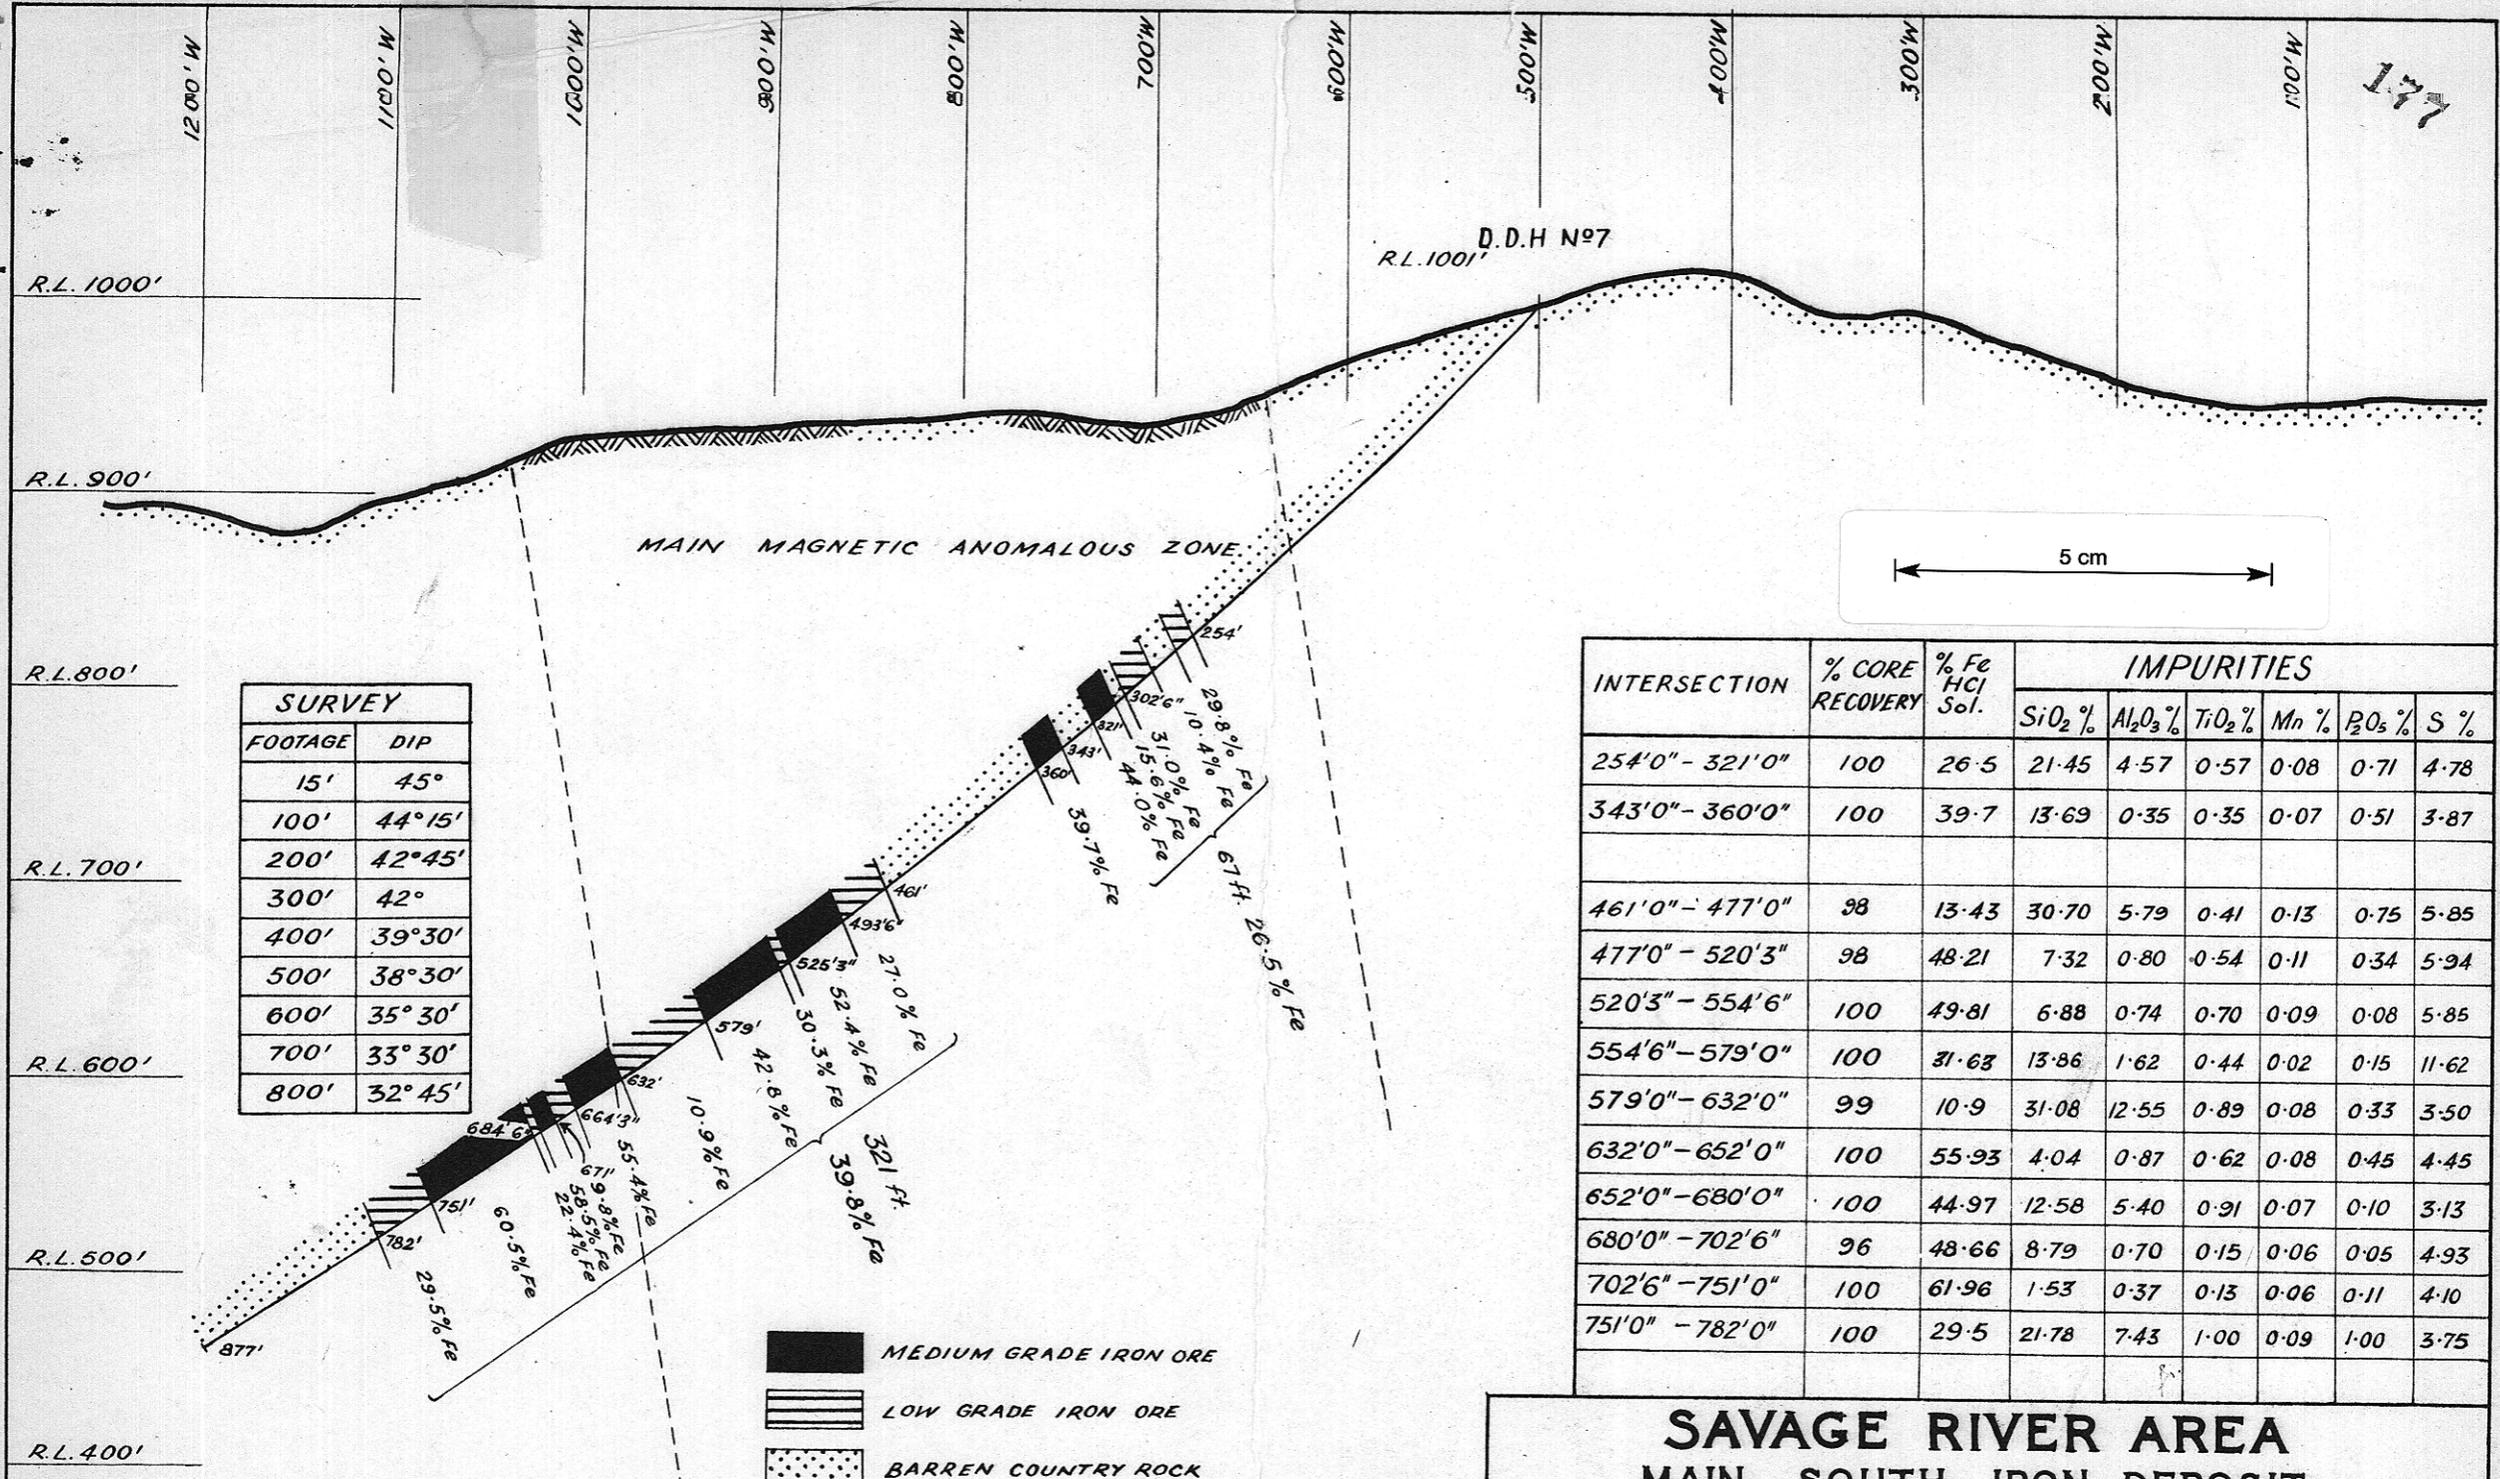

SURVEY	
FOOTAGE	DIP
15'	45°
100'	44° 15'
200'	42° 45'
300'	42°
400'	39° 30'
500'	38° 30'
600'	35° 30'
700'	33° 30'
800'	32° 45'

INTERSECTION	% CORE RECOVERY	% Fe HCl Sol.	IMPURITIES					
			SiO ₂ %	Al ₂ O ₃ %	TiO ₂ %	Mn %	P ₂ O ₅ %	S %
254'0" - 321'0"	100	26.5	21.45	4.57	0.57	0.08	0.71	4.78
343'0" - 360'0"	100	39.7	13.69	0.35	0.35	0.07	0.51	3.87
461'0" - 477'0"	98	13.43	30.70	5.79	0.41	0.13	0.75	5.85
477'0" - 520'3"	98	48.21	7.32	0.80	0.54	0.11	0.34	5.94
520'3" - 554'6"	100	49.81	6.88	0.74	0.70	0.09	0.08	5.85
554'6" - 579'0"	100	31.63	13.86	1.62	0.44	0.02	0.15	11.62
579'0" - 632'0"	99	10.9	31.08	12.55	0.89	0.08	0.33	3.50
632'0" - 652'0"	100	55.93	4.04	0.87	0.62	0.08	0.45	4.45
652'0" - 680'0"	100	44.97	12.58	5.40	0.91	0.07	0.10	3.13
680'0" - 702'6"	96	48.66	8.79	0.70	0.15	0.06	0.05	4.93
702'6" - 751'0"	100	61.96	1.53	0.37	0.13	0.06	0.11	4.10
751'0" - 782'0"	100	29.5	21.78	7.43	1.00	0.09	1.00	3.75

SAVAGE RIVER AREA
MAIN SOUTH IRON DEPOSIT
D.D.H. N°7

320046

0 100 200 FT.

HOLE COMMENCED 27.5.60.
HOLE COMPLETED 13.7.60.
