ENCLOSURE 1.

291133 OR-0298

SAGASCO Resources Ltd.

COMPOSITE LOG
FLINDERS 1

STATE: TASMANIA
BASIN: BASS
PERMIT: T/25P
LOCATION: LAT: 40°22'58.10"
LONG: 145°40'18.690"
SEISMIC LINE: SP 900 TNK4-79

ELEVATION: KB:
DF/RT: 22.3m
WD/GL: 69.25m
TOTAL DEPTH: 2723m R T
STATUS: P & A

DATE SPUDDED: 1000hrs 22/12/92
DATE RIG RELEASED: 1400hrs 22/12/92
DRILLING CONTRACTOR: DIAMOND M. COMPANY
RIG: OCEAN EPOCH
MUDLOG Co: INTERNATIONAL DRILLING FLUIDS PTY.LTD.
CEMENTING Co.: HALLIBURTON

WIRELINE LOGGING: HALLIBURTON
WELLSITE GEOLOGIST: J.REEVE
COMPOSITE LOG: R.J.SUTTILL/J.REEVE
SCALE: 1:500
DRAWN: P.OLDHAM
DRAWING No: BAS00.9962

LOCATION

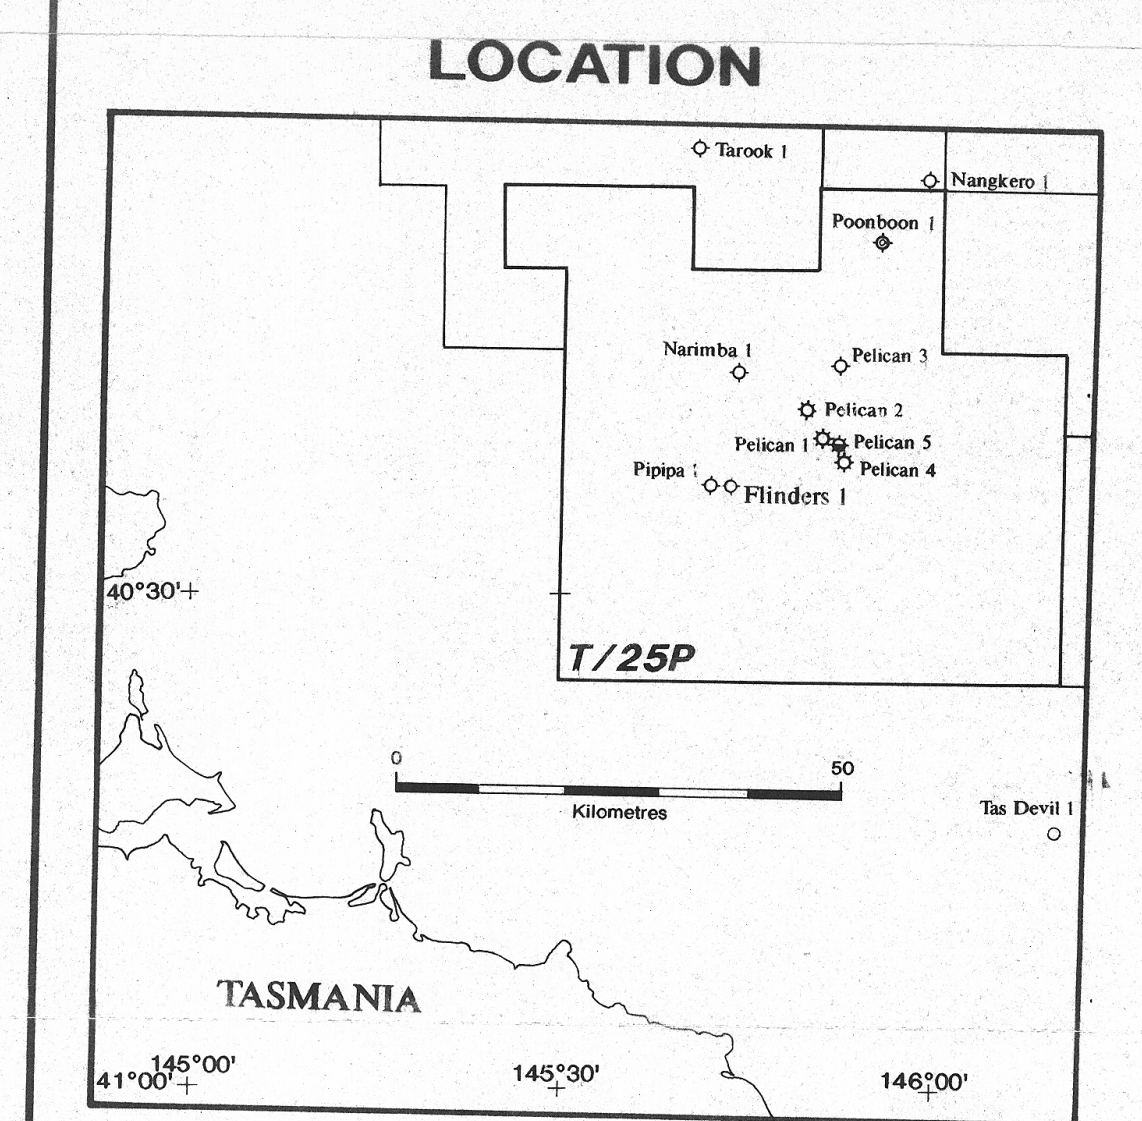

LEGEND

SYMBOLS

- DRILL STEM TEST
- CASING SHOE
- CEMENT PLUG
- Rec / Not Rec SIDEWALL CORES
- ⊙ DEVIATION SURVEY
- RFT TEST POINT
- PALYNOLOGY
- (0.7) VITRINITE REFLECTANCE

LITHOLOGY

- SANDSTONE
- SHALE
- CLAYSTONE
- MARL
- SILTSTONE
- LIMESTONE
- ■ COAL
- INTRUSIVE
- DOLOMITE

p – Pyrite
g – Glauconite
A – Arkosic to feldspathic
V – Tuffaceous
M – Mica
T – Calcareous

WELL SYMBOLS

- ● OIL
- OIL SHOW
- ☼ GAS
- GAS SHOW

5 cm

LOGGING

LOG	RUN	INTERVAL (M)	MAX TEMP
DLL-MSFL-LSS-GR-SP-DTD-CAL	1A	1243-405.8m Did not reach TD GR to mudline	48.3°C
HRI-MSFL-LSS-GR-SP-DTD-CAL	2A	2716.1-1525.2m	116.7°C
SDL-DSN-CSNG-DTD-CAL	2B	2707.8-1525.2m	123.3°C
SED-GR	2C	2716.5-1525.2m	126.1°C
VSP	2D	2705-305m	–
SWC-GR	2E	Abandoned	

ENGINEERING DATA

HOLE SIZE			CEMENT PLUGS		
SIZE	FROM	TO	FROM	TO	CEMENT
914mm (36")	SEA FLOOR	127.6m RT	2300m RT	2177m RT	140 sx
445mm (17 1/2")	127.6m RT	408.0m RT	1550m RT	1470m RT	130 sx
311mm (12 1/4")	408.0m RT	1525.0m RT	125m RT	105m RT	50 sx
216mm (8 1/2")	1525.0m RT	2723.0m RT			

CASING

SIZE	WEIGHT	GRADE	DEPTH	CEMENT	CEM'D TO
762mm (30")	310 ppf	B	124.50m RT	700 sx	SEA FLOOR
340mm (13 3/8")	68 ppf	K-55	403.00m RT	498 sx	SEA FLOOR
244mm (9 5/8")	47 ppf	N-80	1519.98m RT	240 sx	SEA FLOOR
