343128

OR. 340

OFFSHORE 26

ENCLOSURE 18c

Schlumberger

ISF/

COUNTY AUSTRALIA
FIELD or LOCATION WILDCAT
WELL NARIMBA 1
COMPANY ESSO

COMPANY ESSO AUSTRALIA LTD.
WELL NARIMBA 1
FIELD WILDCAT
COUNTY AUSTRALIA STATE TASMANIA
LOCATION LAT: 40° 16' 16.153" S. LONG: 145° 43' 53.327" E.
Sec. Twp. Rge.
Other Services: SLK, HDT FDC/CNL/GR ST.

Permanent Datum: MSL , Elev. 0
Log Measured From KB , 32 Ft. Above Perm. Datum
Drilling Measured From KB.
Elev.: K.B. 32
D.F. 31
G.L. -253

FIELD PRINT

Date	OCT. 1. 1973				
Run No.	5, 5" 2"				
Depth—Driller	11003				
Depth—Logger	10993				
Btm. Log Interval	10986				
Top Log Interval	10250				
Casing—Driller	9 5/8 @ 8808	@	@	@	
Casing—Logger	8789				
Bit Size	8 1/2				
Type Fluid in Hole	LIGNOSULFONATE				
Dens. | Visc.	11.0 | 44				
pH | Fluid Loss	9.8 | 4.4 ml	ml	ml	ml	
Source of Sample	FLOWLINE				
Rm @ Meas. Temp.	0.80 @ 69 °F	@ °F	@ °F	@ °F	
Rmf @ Meas. Temp.	0.56 @ 68 °F	@ °F	@ °F	@ °F	
Rmc @ Meas. Temp.	1.17 @ 68 °F	@ °F	@ °F	@ °F	
Source: Rmf | Rmc	PRESS				
Rm @ BHT	0.21 @ 264 °F	@ °F	@ °F	@ °F	
Time Since Circ.	7 1/2 HRS				
Max. Rec. Temp.	264/265 °F	°F	°F	°F	
Equip. | Location	2080 | SAL				
Recorded By	CHAFFE/CLARKE				
Witnessed By	SVALBE				

FOLD HERE The well name, location and borehole reference data were furnished by the customer.

Date	OCT. 1 1973					
Run No.	5, 5" 2"					
Depth—Driller	11003					
Depth—Logger	10993					
Btm. Log Interval	10986					
Top Log Interval	10250					
Casing—Driller	9 5/8 @ 8808	@	@	@	@	@
Casing—Logger	8789					
Bit Size	8 1/2					
Type Fluid in Hole	LIGNOSULFONATE					
Dens. | Visc.	11.0 | 44					
pH | Fluid Loss	9.8 | 4.4 ml	ml	ml	ml	ml	ml
Source of Sample	FLOWLINE					
Rm @ Meas. Temp.	0.80 @ 69 °F	@ °F	@ °F	@ °F	@ °F	@ °F
Rmf @ Meas. Temp.	0.56 @ 68 °F	@ °F	@ °F	@ °F	@ °F	@ °F
Rmc @ Meas. Temp.	1.17 @ 68 °F	@ °F	@ °F	@ °F	@ °F	@ °F
Source: Rmf | Rmc	FLOWLINE					
Rm @ BHT	0.21 @ 264 °F	@ °F	@ °F	@ °F	@ °F	@ °F
Time Since Circ.	7 1/2 HRS					
Max. Rec. Temp.	264/265 °F	°F	°F	°F	°F	°F
Equip. | Location	2080 | SAL					
Recorded By	CHAFFE/CLARKE					
Witnessed By	SVALBE					

Changes in Mud Type or Additional Samples

Date | Sample No.			
Depth—Driller			
Type Fluid in Hole			
Dens. | Visc.			
ph | Fluid Loss	ml		
Source of Sample			
Rm @ Meas. Temp.	@ °F	@ °F	
Rmf @ Meas. Temp.	@ °F	@ °F	
Rmc @ Meas. Temp.	@ °F	@ °F	
Source: Rmf | Rmc			
Rm @ BHT	@ °F	@ °F	
Rm @ BHT	@ °F	@ °F	
Rm @ BHT	@ °F	@ °F	

Scale Changes

Type Log	Depth	Scale Up Hole	Scale Down Hole

Run No.	5
Ind. Panel No.	A-136
Mem. Panel No.	VA-53
Ind. Cart. No.	HA-123
Ind. Sonde No.	S-124
Sonic Panel No.	
Oscil. Panel No.	
Sonic Cart. No.	
Sonic Sonde No.	
G.R. Cart. No.	
G.R. Panel No.	
Caliper No.	
TTR No.	
S.E.	6.4
SBR	1
Cent. Device	
Stand off-Inches	1 1/2"
Time Const.-Sec.	
Speed-F.P.M.	

REMARKS:

5 cm

Service Order No.-
API Serial No.-
Check one, filling in blanks where applicable:
☒ Surface determined sonde errors used for 6FF40.
☐ 6FF40 sonde error corrected for inch borehole signal at Rm
☐ 6FF40 zero set in hole at depth of feet.

SPONTANEOUS-POTENTIAL millivolts	DEPTHS	RESISTIVITY ohms - m²/m	CONDUCTIVITY millimhos/m = 1000/ohms-m²/m
10 — |↔| +	2"	SPHERICALLY FOCUSED 0 20 0 200 INDUCTION 0 20 AMP SFL 0 4	6 FF40 INDUCTION 1000 0

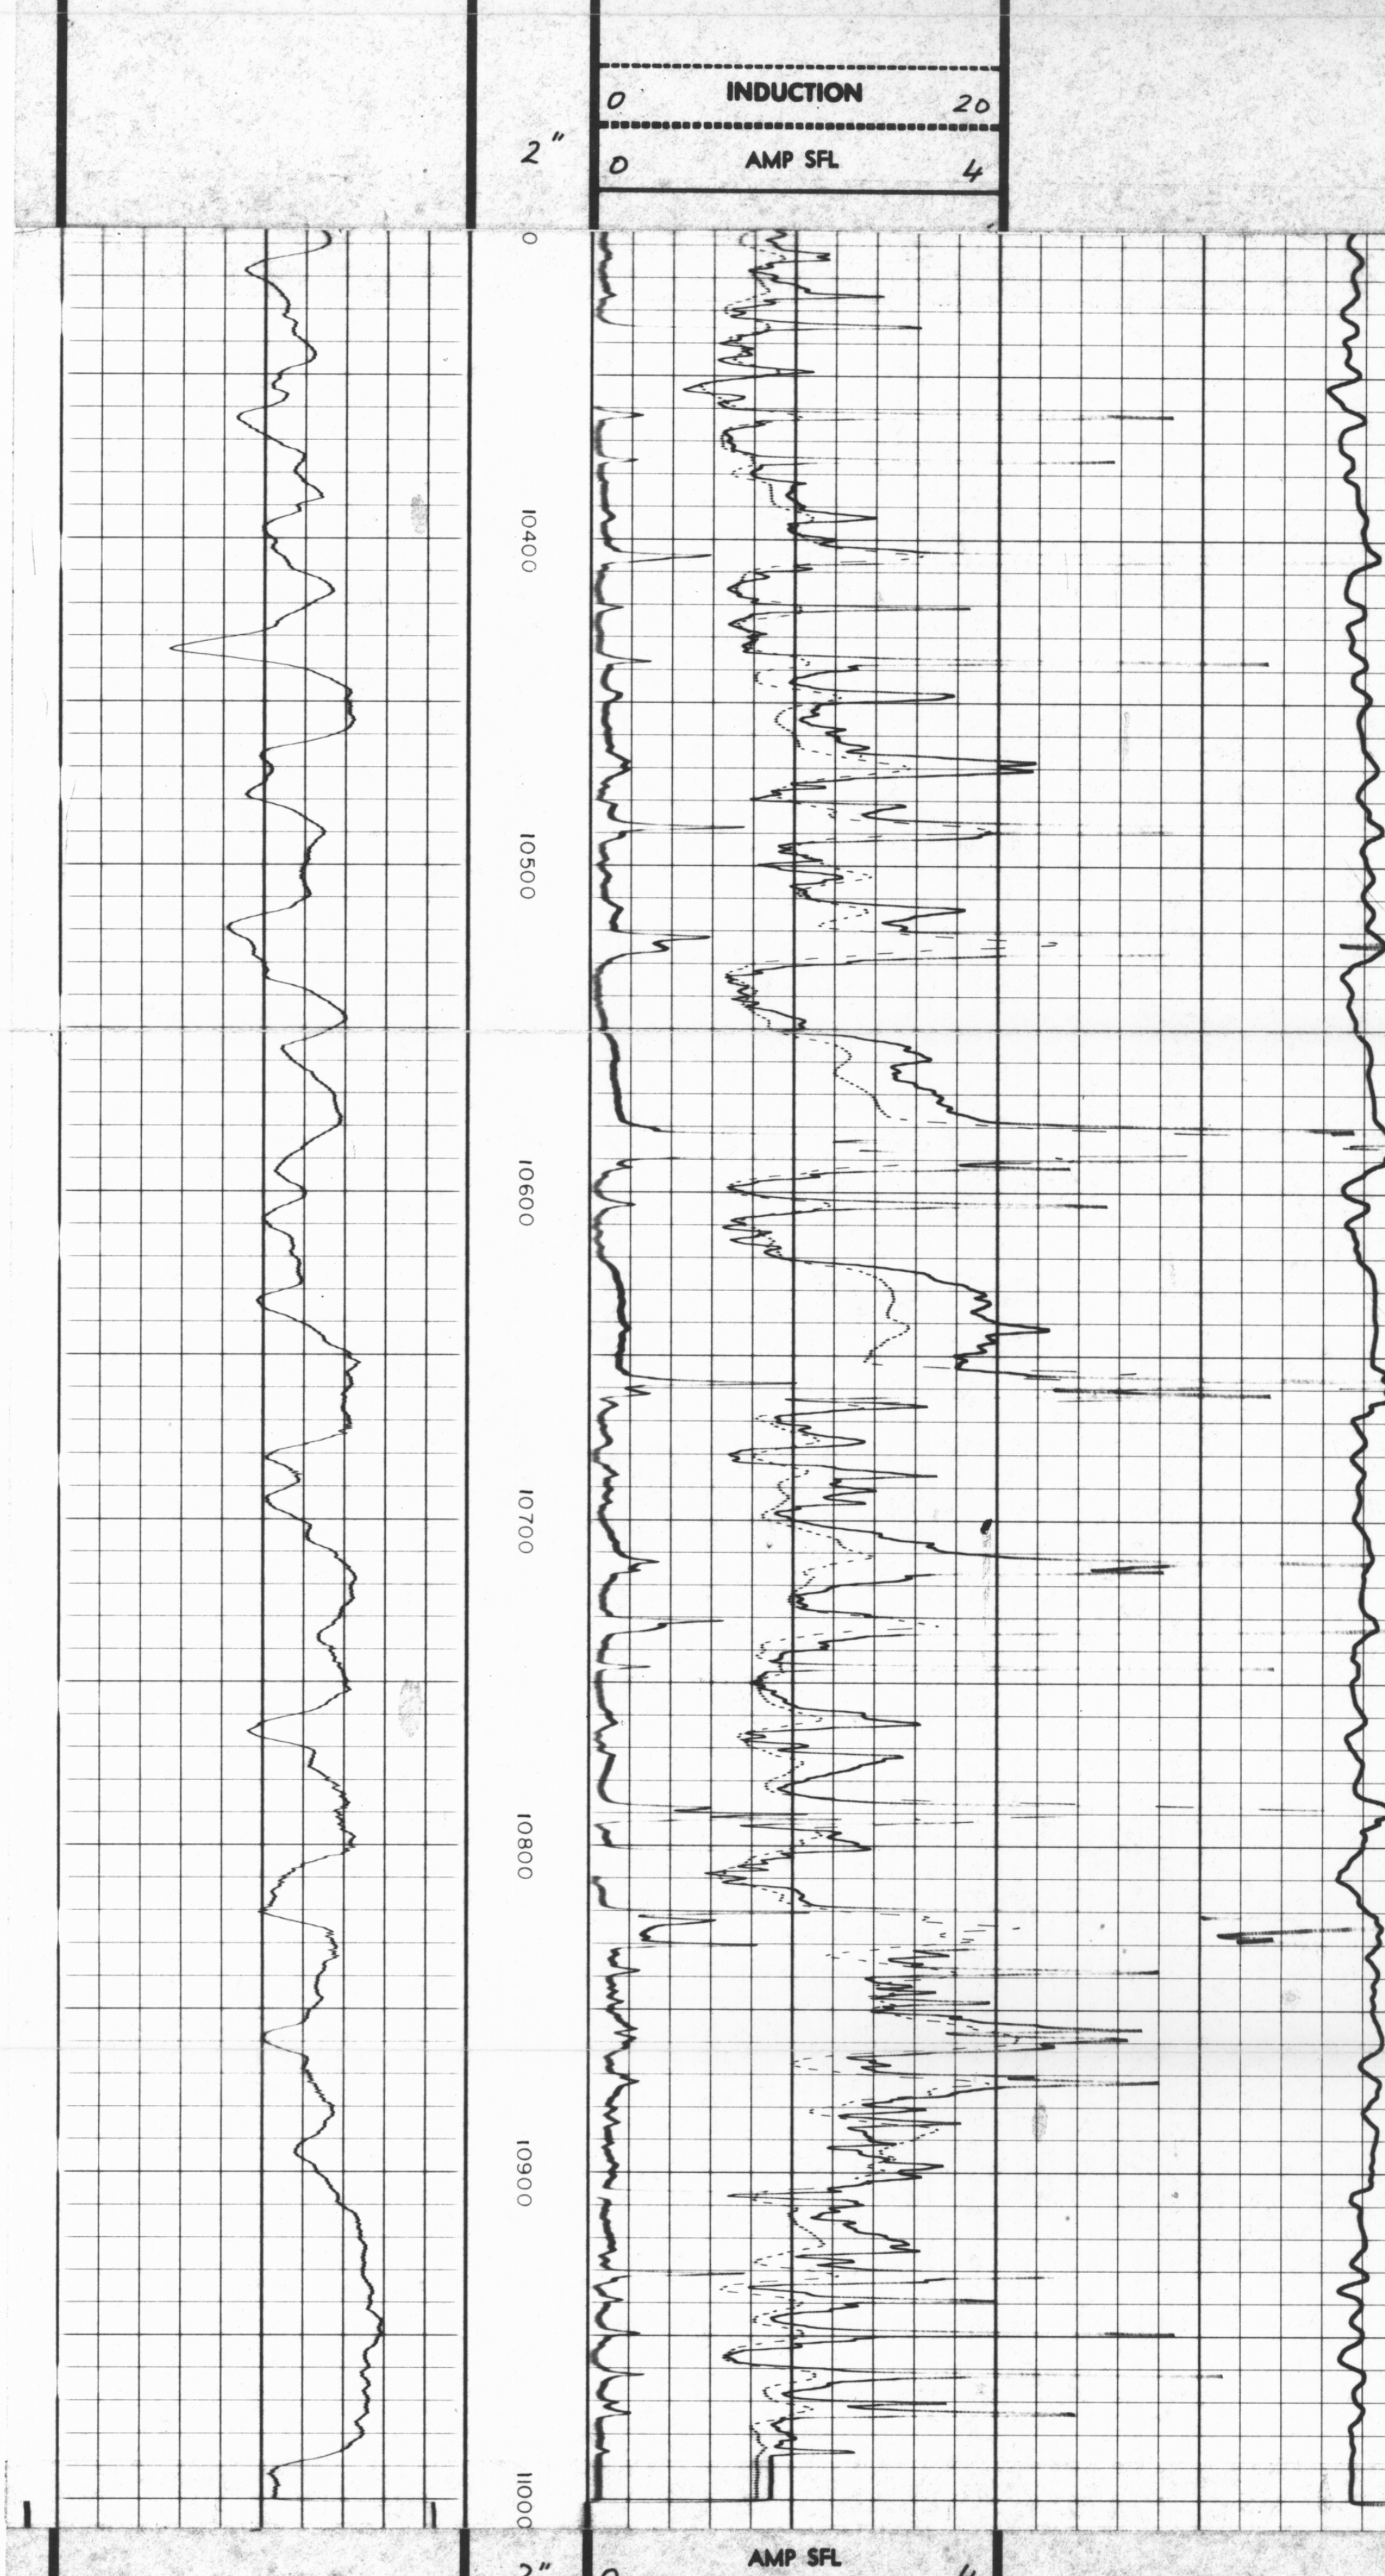

10 — |↔| +	2"	AMP SFL 0 4 SPHERICALLY FOCUSED 0 20 0 200 INDUCTION 0 20	6 FF40 INDUCTION 1000 0
SPONTANEOUS-POTENTIAL millivolts	DEPTHS	RESISTIVITY ohms - m²/m	CONDUCTIVITY millimhos/m = 1000/ohms-m²/m

COMPANY ESSO AUSTRALIA LTD.
WELL NARIMBA 1
FIELD WILDCAT
COUNTY AUSTRALIA STATE TASMANIA

SCHL. FR 10986
SCHL. TD 10993
DRLR TD 11003
Elev:
KB 32
DF 31
GL -253

SPONTANEOUS-POTENTIAL MILLIVOLTS

DEPTHS

10 — |↔| +

RESISTIVITY OHMS = M²/M

INDUCTION — 6FF40
SPHERICALLY FOCUSED

5"

0.2 1.0 10 100 1000 2000

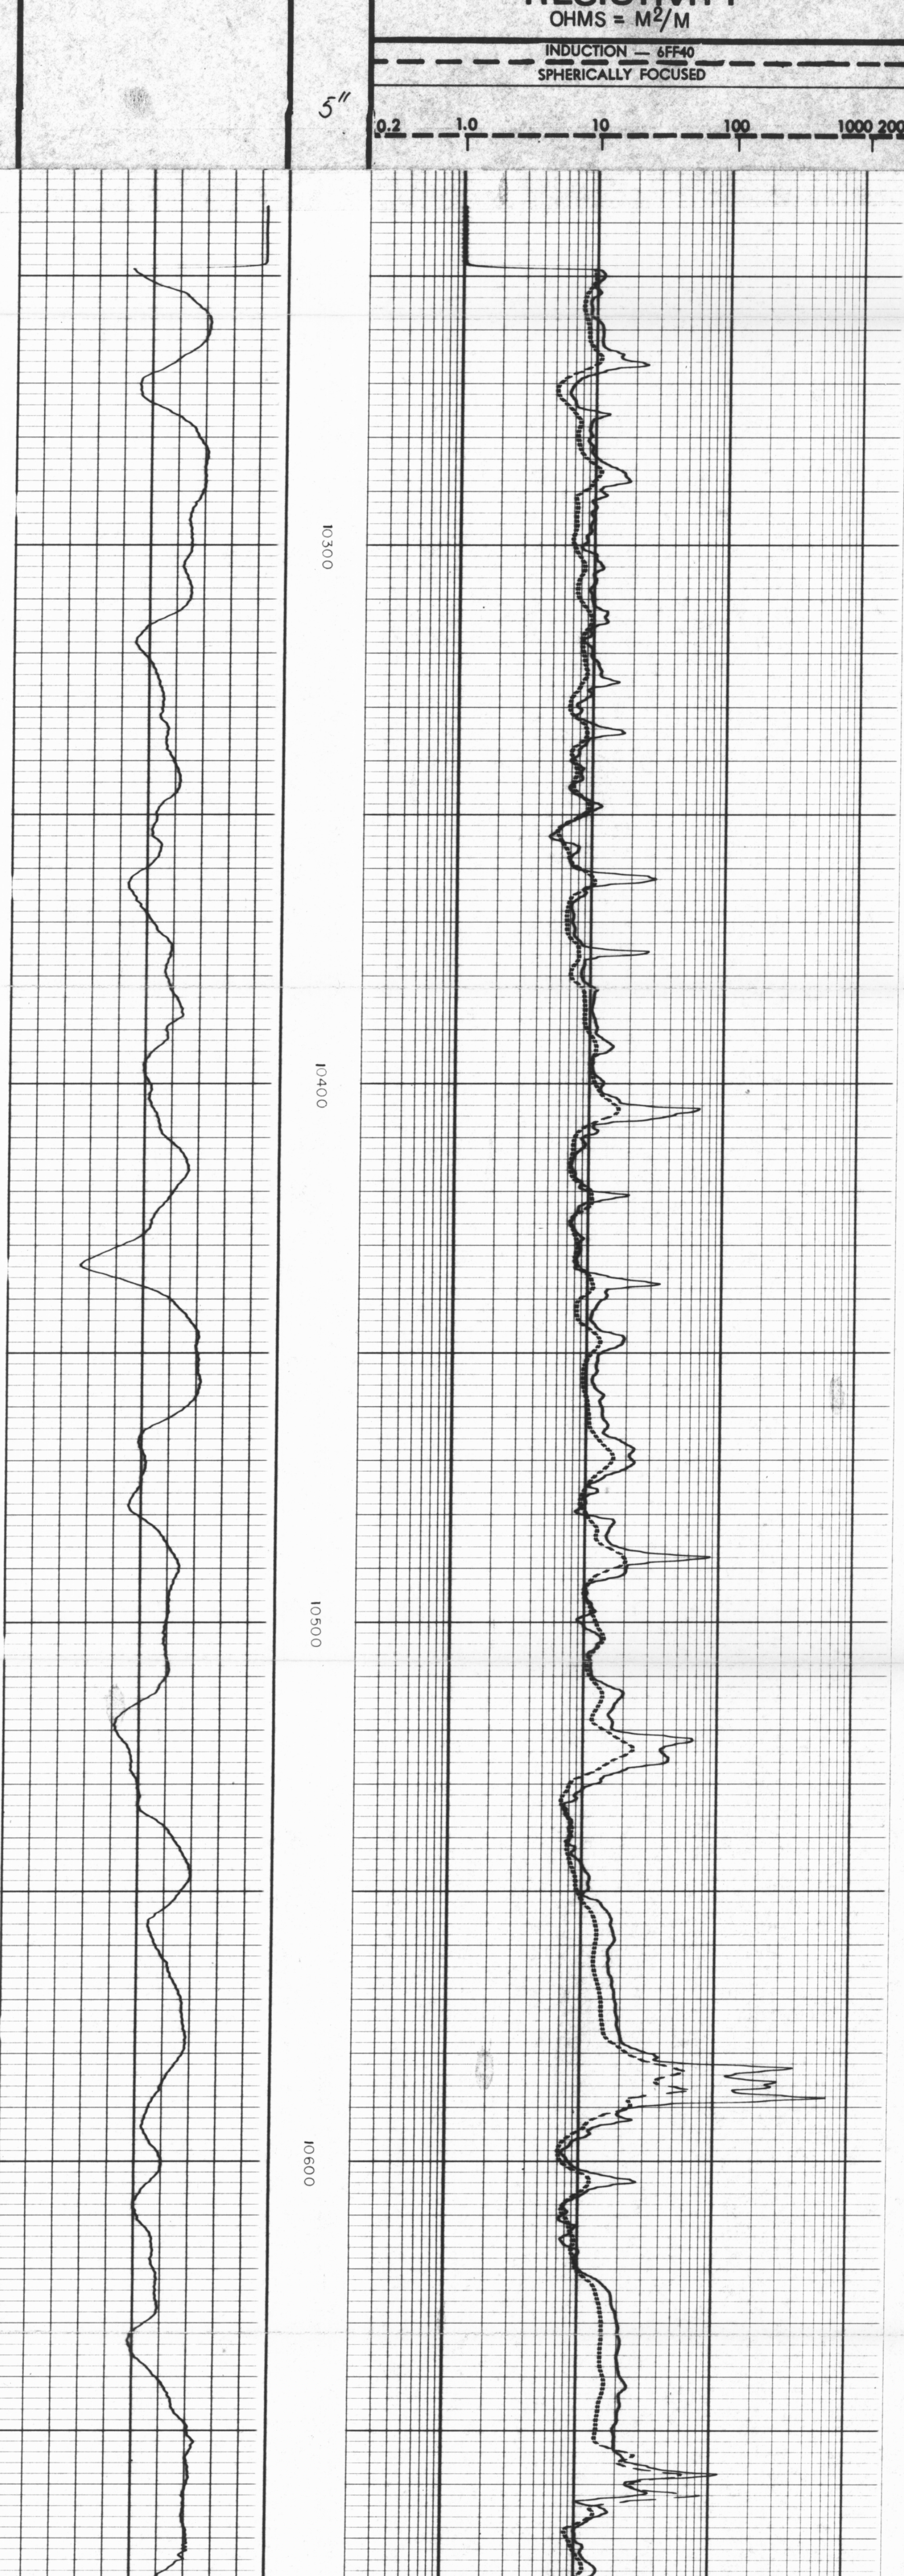

5"

0.2 1.0 10 100 1000 2000

INDUCTION — 6FF40
SPHERICALLY FOCUSED

RESISTIVITY OHMS = M²/M

10 — |↔| +

SPONTANEOUS-POTENTIAL MILLIVOLTS

DEPTHS

COMPANY ESSO AUSTRALIA LTD.
WELL NARIMBA 1
FIELD WILDCAT
COUNTY AUSTRALIA STATE TASMANIA

SCHL. FR 10986
SCHL. TD 10993
DRLR TD 11003
Elev:
KB 32
DF 31
GL -253

CALIBRATION DATA

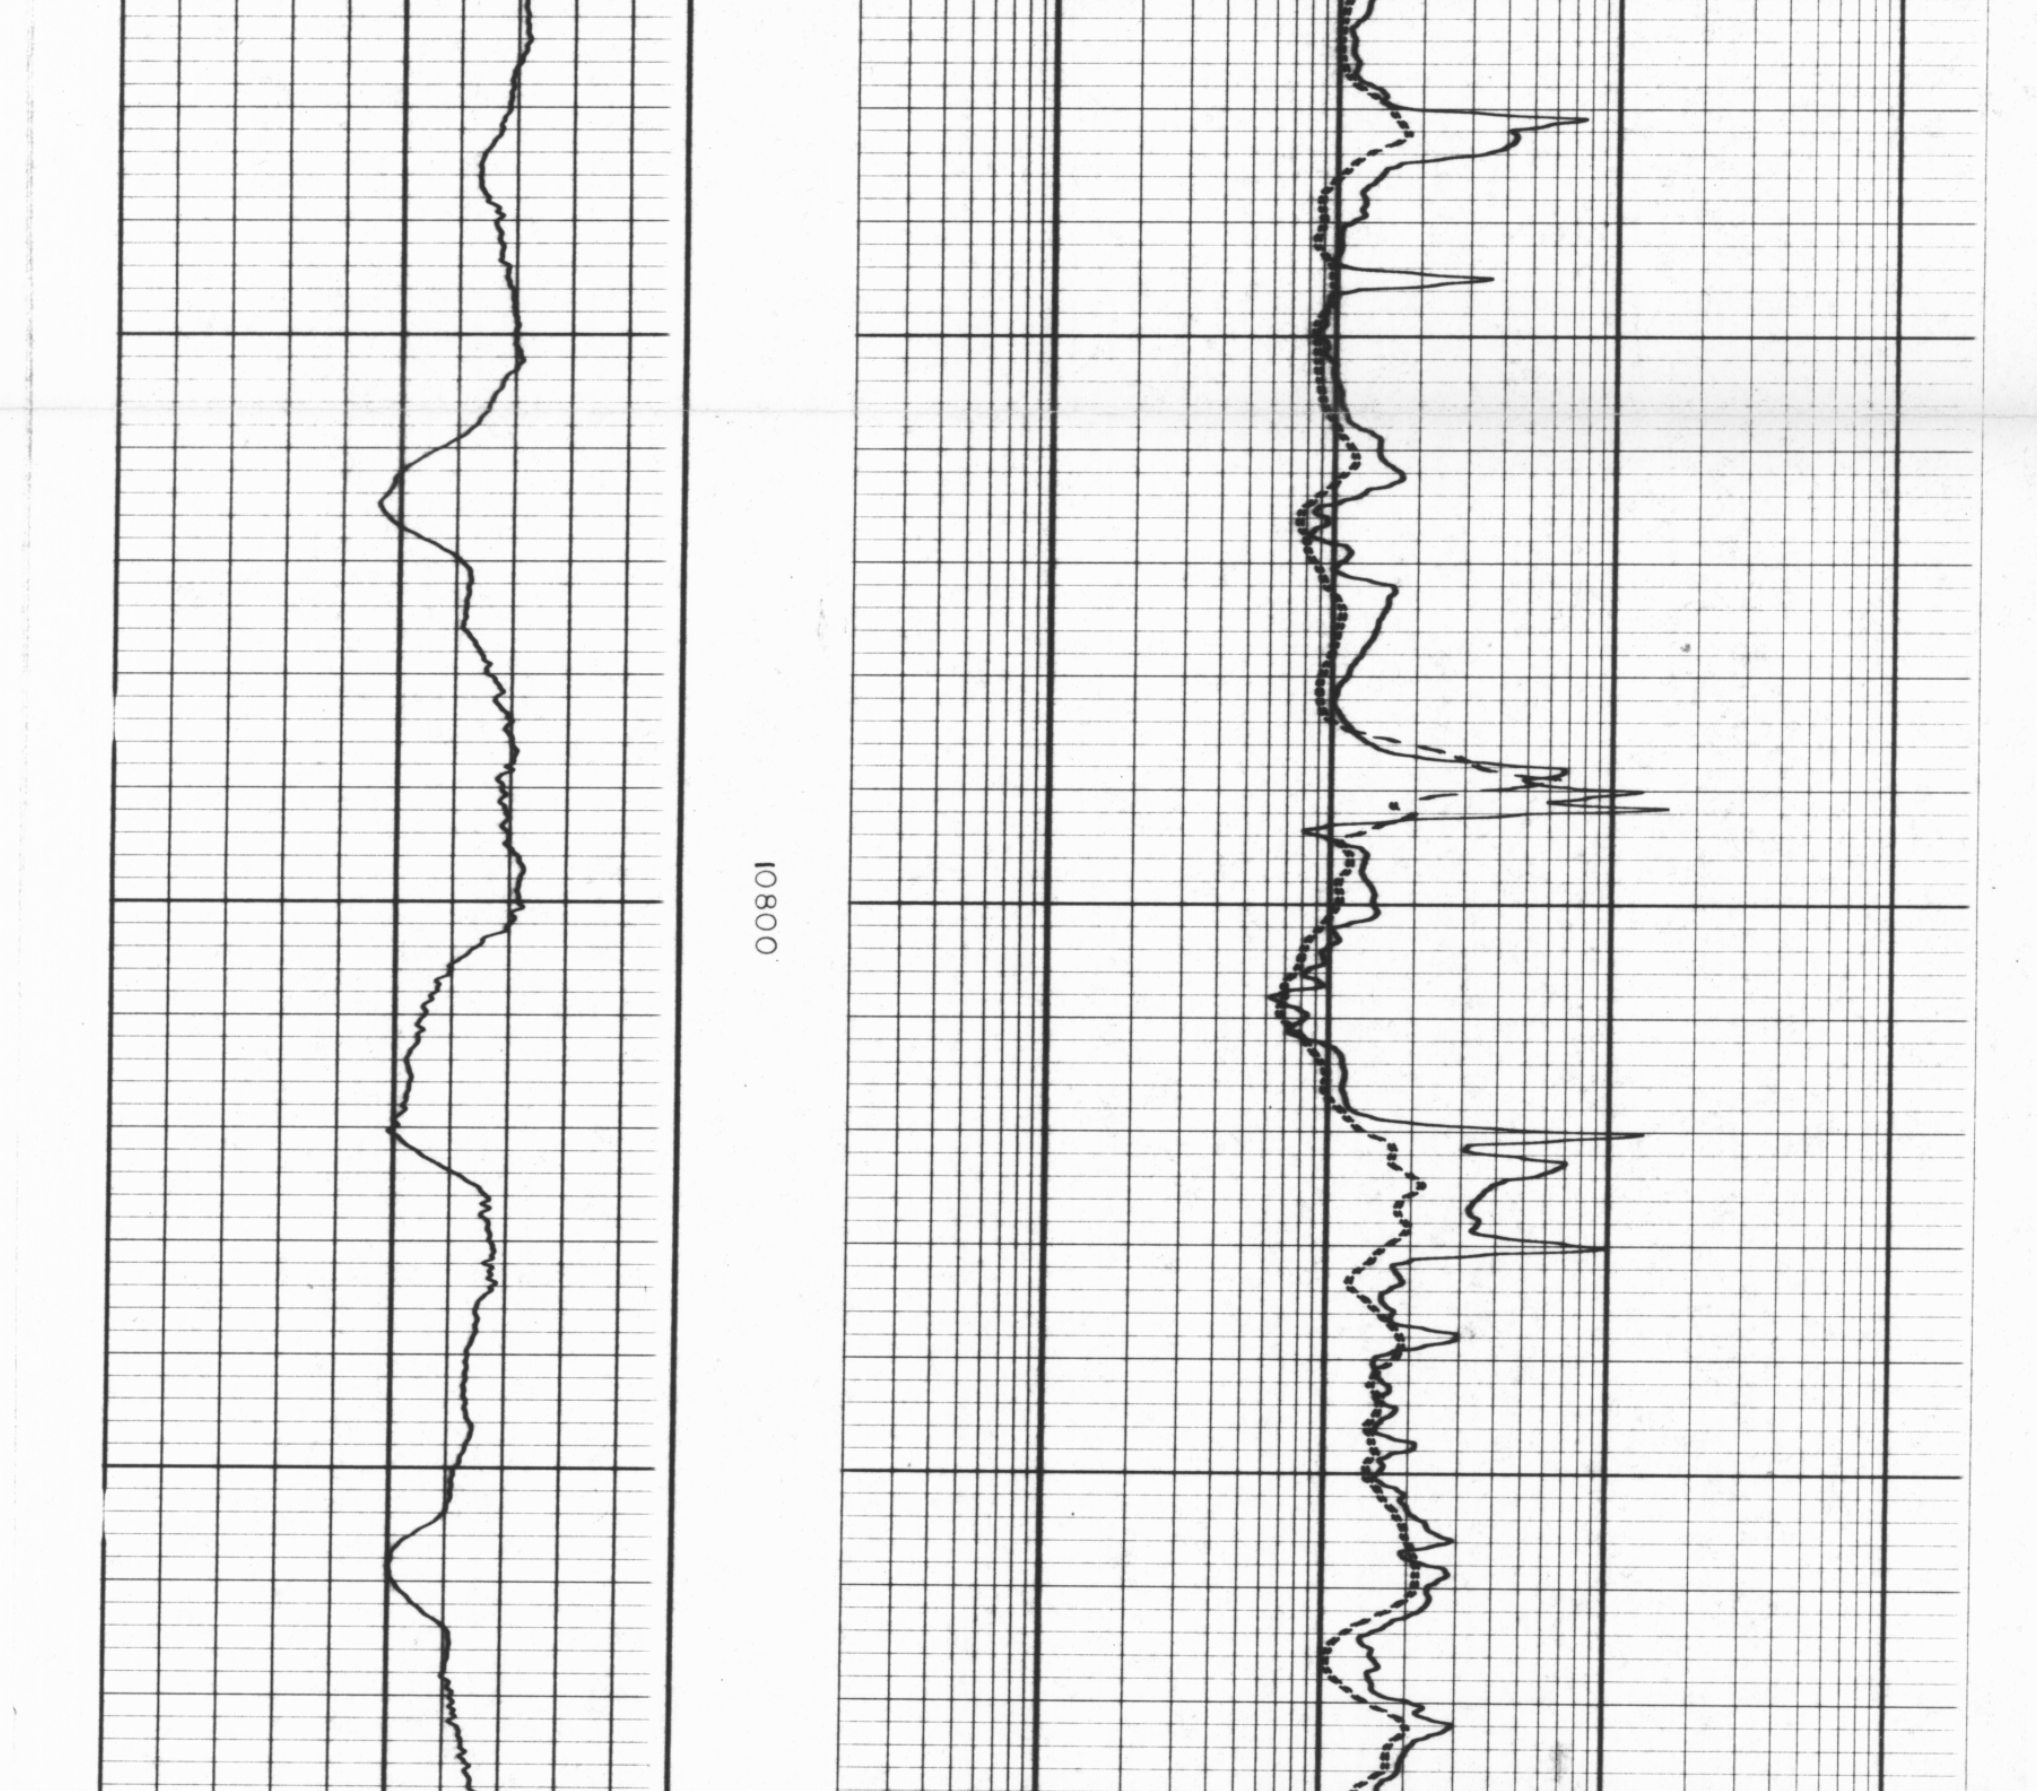

MASTER CALIBRATION
ILP-A 136
IAP-VA 53
IAS-S 124
ITL-0 160
IAC-HA 123

Test Loop Signal
Sonde Error
2 Ω-M
500 Ω-M
100
1
Mechanical Zero

REPEAT SECTION

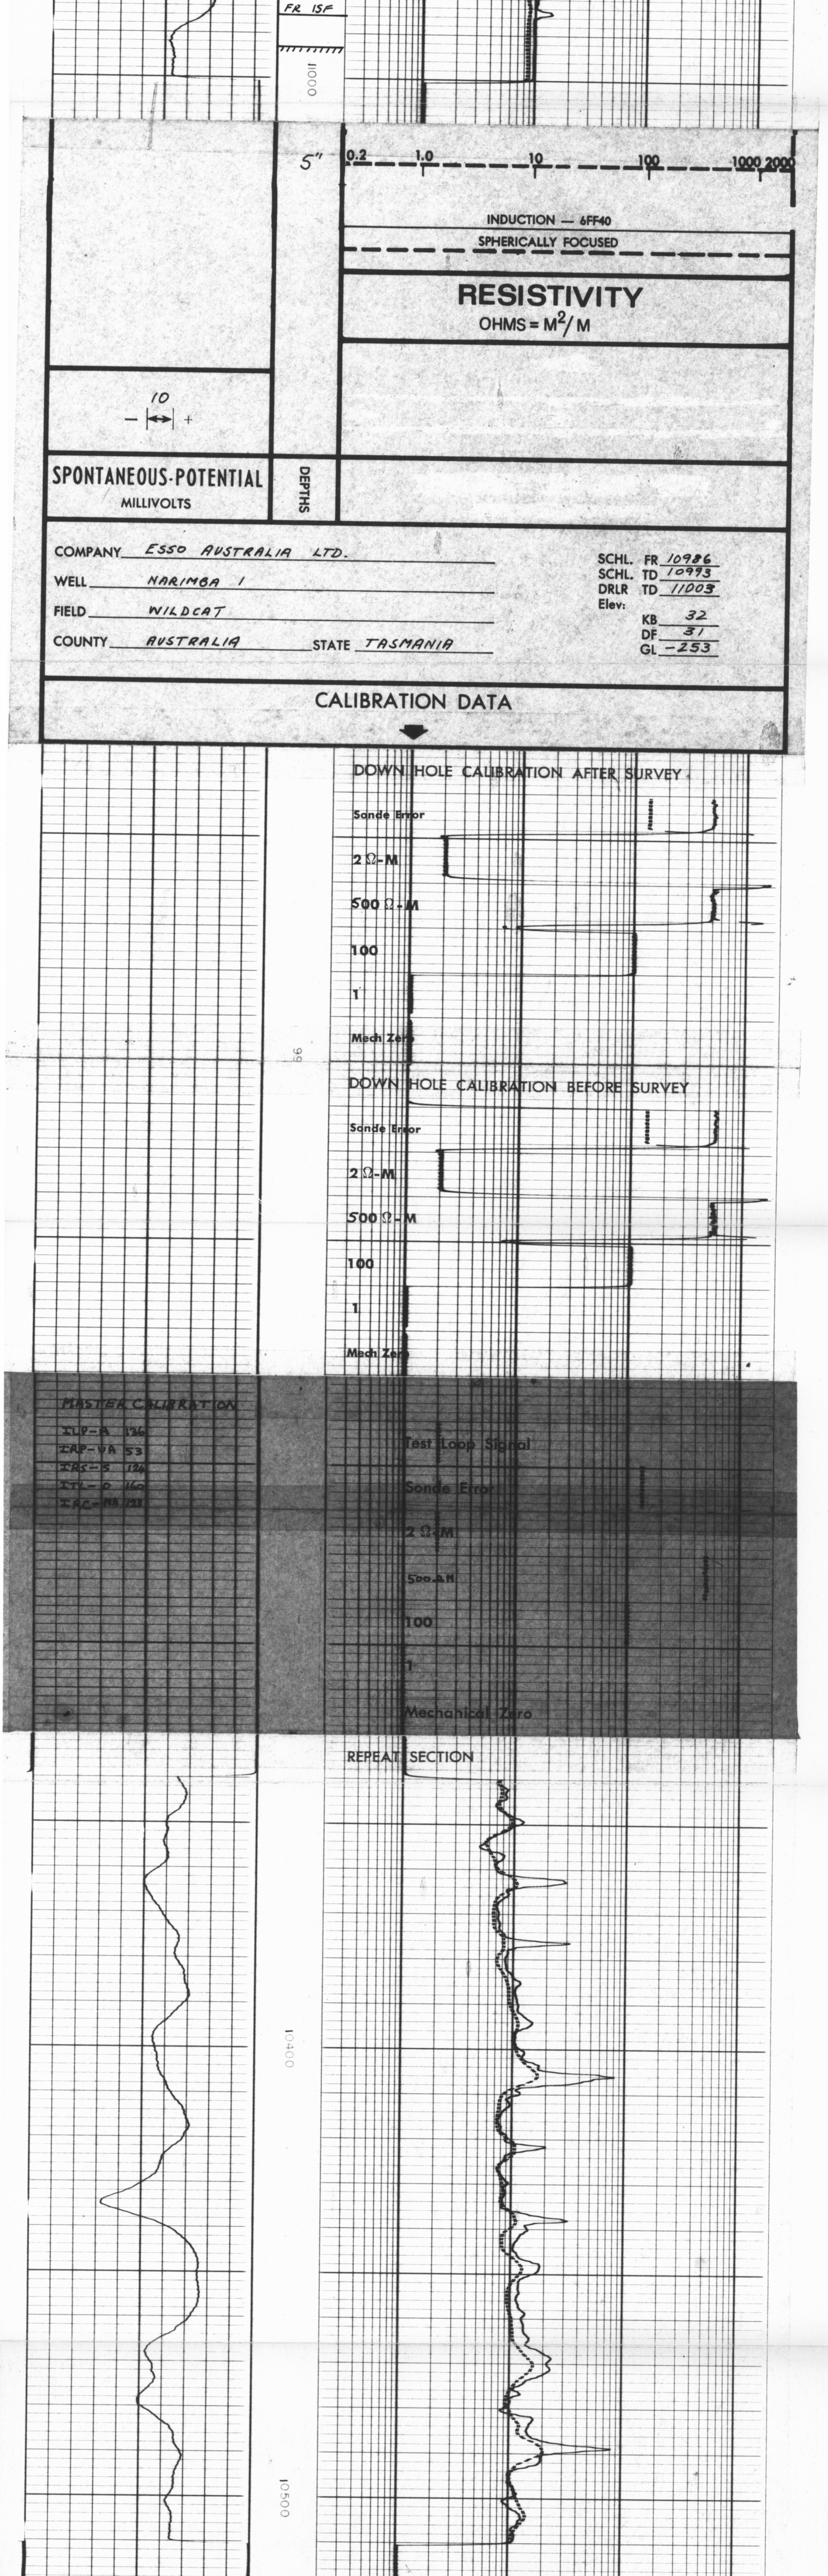

CALIBRATION DATA

5 cm

COMPANY ESSO AUSTRALIA LTD.
WELL NARIMBA 1.
FIELD WILDCAT.
COUNTY AUSTRALIA STATE TASMANIA.

SCHL. FR 10986
SCHL. TD 10993
DRLR TD 11003
Elev:
KB 32
DF 31
GL -253
