ENCL. 99

467107

OR-0359

SCHLUMBERGER

MICROLATEROLOG

COUNTRY	AUSTRALIA
FIELD	WILDCAT
WELL	BASS 1
COMPANY	ESSO

COMPANY ESSO EXPLORATION AUST. INC.
WELL BASS 1
FIELD WILDCAT
COUNTRY AUSTRALIA STATE TAS.

Location : 39° 46' 18" S 145° 44' 03" E

Other Services : IES,SONIC,CDM

Ref. No

Permanent Datum Mean Sea Level Elev.: 0'
Log Measured From RT 31 Ft. Above Perm. Datum
Drilling Measured From RT 31 Ft. Above Perm. Datum

Elev.: K.B.
D.F. 31
G.L.

RUN No. | Depth Scale	1 | 5"	|	|
Date	6th.August,1965		
First Reading	2300		
Last Reading	770		
Interval Measured	1530		
Casing Schlumberger	770		
Casing Driller	768		
Depth Reached	2301		
Bottom Driller	2304		
Mud Nature	Bentonite		
Density | Viscosity	10.1 | 43	|	|
Mud Resistivity	.60 @ 66 °F	@ °F	@ °F
Mud Resistivity BHT	.39 @ 104 °F	@ °F	@ °F
pH | Fluid Loss	10.3 | 12 CC/30 min.	| CC/30 min.	| CC/30 min.
Origin of Sample	Flowline		
Rmf	.46 @ 61 °F	@ °F	@ °F
Rmc	1.69 @ 61 °F	@ °F	@ °F
Bit Size 1	12¼ To TD	To	To
2	To	To	To
Casing Size	20"		
Operating Rig Time	2½hrs		
Truck No.	2035		
Recorded By	I Strecker		
Witness	W Nixon		

FOLD HERE

REMARKS : Wave Compensating Device used Wind 25mph Waves 8-12'

5 cm

RECORDING DATA			
Run No.	1		
Origin of filtrate	press		

EQUIPMENT DATA			
Run No.	1		
Panel No	TMP-E 185		
Cartridge No	TMC-E 214		
Sonde No	PML-B 26		
Pad Type	V111		

MICROCALIPER Inches	DEPTHS	RESISTIVITY ohms - m²/m	RESISTIVITY ohms - m²/m
6 16		0 100	0 20

MICROCALIPER Inches	DEPTHS	RESISTIVITY ohms - m²/m	RESISTIVITY ohms - m²/m
6 16		0 100	0 20

COMPANY ESSO EXPLORATION AUST. INC.
WELL BASS 1
FIELD WILDCAT
COUNTRY AUSTRALIA STATE VICT.

SCHL. F.R. 2300
SCHL. T.D. 2301
DRLR. T.D. 2304

CALIBRATION FILMS

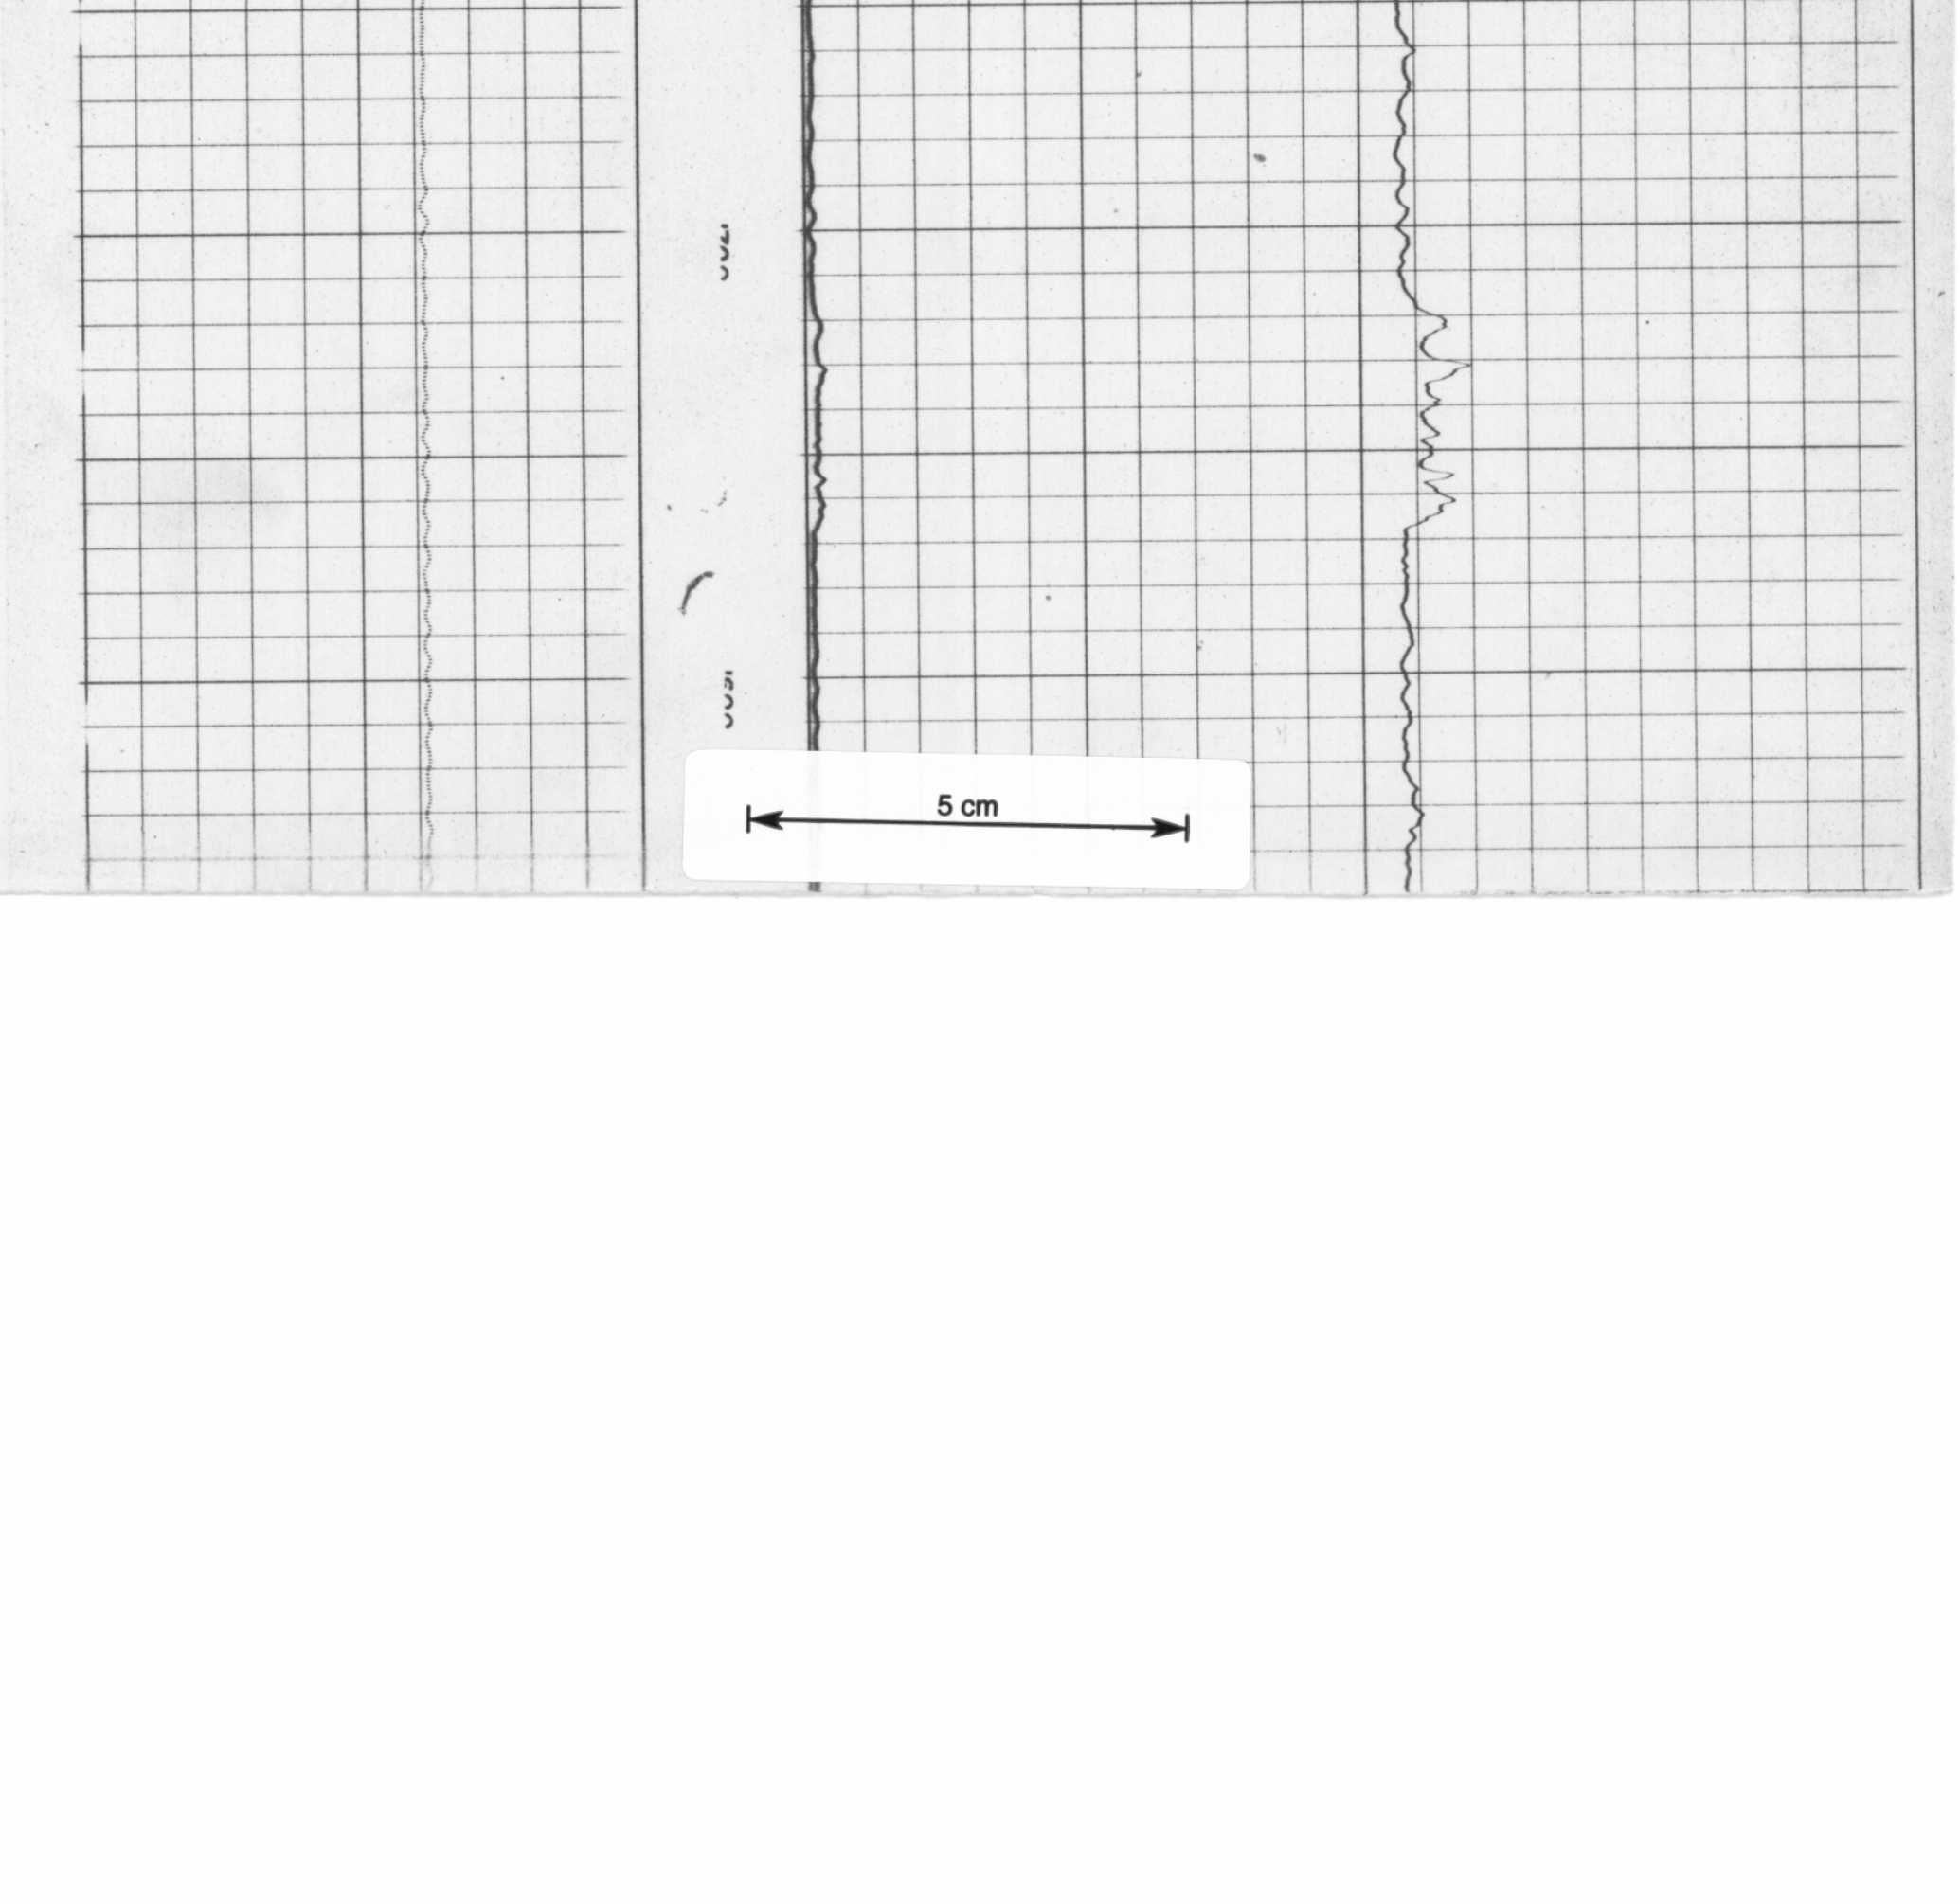

MUD LOG

5 cm
